


October 5 - 9, 2015

Engineering Division:

- 1) North Avenue Drainage Project ongoing – Contractor addressing punchlist work;
- 2) Pond Brook Circle Drainage Project ongoing – Drainage excavation and installation ongoing;
- 3) Wellesley Street at Brown Street Signal Project ongoing – Signal is operational;
- 4) Black Oak Pump Station Project ongoing – Pressure and other testing completed. Station startup. Gas relay began anticipate two to three weeks to complete main and service work. Work still remaining is installation of backup generator, tank removal, pavement work and landscaping awaiting electric company to remove existing pole and service;
- 5) Various Locations (Pine Street, Highland Street/Winter Street, and Summer Street) Drainage Project – Pine Street drainage 90% completed. Highland Street/Winter Street drainage 90% completed with landscaping and wall work ongoing. Portion of Summer Street drainage work completed; remaining portion working on easement rights;
- 6) Solar PV Project – Solar array construction underway. Anticipated deliveries throughout month of October;
- 7) Old Colony Road Water Main Project (FY16) – Proposal to be advertised in February 2016;
- 8) Overseeing consultants' work on several sidewalk feasibility studies (Merriam Street, Highland Street, and Warren Avenue) – Feasibility plans available for viewing on-line;
- 9) Overseeing consultant's work on the study of the Ash Street / Route 30 / Fire Station Intersection;
- 10) Overseeing consultant's work on the modification of the Boston Post Road / Wellesley Street intersection study and the Boston Post Road / School Street intersection study;
- 11) Finalizing consultant proposal for the Paines Hill Water Tank Improvement Project;
- 12) Brown Street Sidewalk Project advertised. Bid Opening September 17th. Evaluating bids and funding;

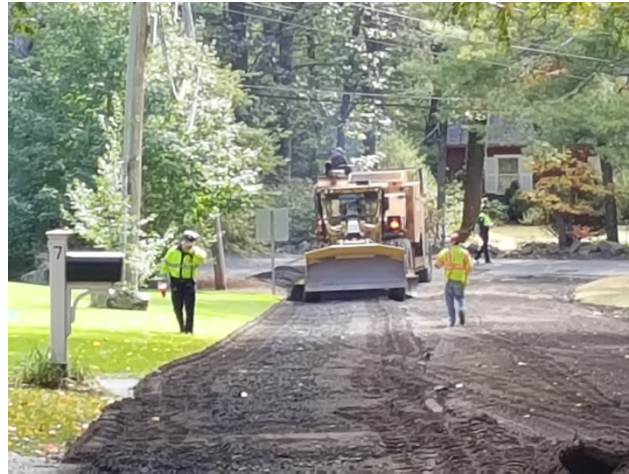

- 13) Route 30 (South Avenue) and Wellesley Street Signal Improvement Project advertised September 19th. Anticipated bid opening on December 15, 2015;
- 14) Currently reviewing 9 Stormwater Permits;
- 15) Currently issued 26 Stormwater permits which also requires construction inspection;

Water Division:

- 1) Completed approximately 35 Dig Safe inspections;
- 2) Performed weekly water samples (4) and station/tank inspections;
- 3) Conducted five final meter reads;
- 4) Completed work required via DEP Sanitary Survey;
- 5) Continued to work on water billing;
- 6) Installed new fire hydrant and extended water main on Wildwood Lane prior to roadway reconstruction;
- 7) Oversaw Black Oak Pump Station work. New station startup;

Park and Cemetery Division:

- 1) Mowed and trimmed approximately 20 acres of cemetery and park land;
- 2) Loamed and seeded various areas in Linwood Cemetery;
- 3) Maintained planting beds and newly planted trees;
- 4) Officiated three committal services.

Solid Waste and Recycling Division:

- 1) Processed approximately 23 tons of solid waste and 19 tons of recycling;
- 2) Picked up trash and recycling at various town buildings;
- 3) Policed Transfer Station for litter;
- 4) Ongoing Voluntary Pilot PAYT Program;
- 5) Assisted the Park and Cemetery Division with grounds maintenance;
- 6) Coordination with the Solar Array project.

Highway/Stormwater Divisions:

- 1) Preparing fiscal year 2016 roadway reconstruction roadways (e.g. lowering structures, saw cutting joints, etc.).
